

# South Dakota Shooting Sports Complex


**South Dakota Game, Fish and Parks**

*Presentation to the Joint Appropriations Committee*

*November 14, 2024*



# Project Status



## PHASE I

Dakota Redi Mix is continuing the dirt work portion of the project.

DRM is anticipated to meet the substantial completion date of 11/15/24 with the potential for punch list items to be addressed by the final completion date of 11/29/24.



## PHASE II

McGough was the low bid on the structure/utilities/finish work portion of the project

Drilling of the water well has been completed, testing for quality and quantity is anticipated in mid-November

Geothermal wells have been completed

Primary electric has been brought into the south site and will continue installation on the north site

Secondary utilities (electric and water lines) are being installed throughout the site

Concrete pads at all 50/100-yard ranges has been placed and lumber for the shooting structures is on site

The Hunting and shooting education building underground plumbing has been completed and inspected, footings and foundation walls are currently being placed and the slab is anticipated to be placed mid-November

The expected final completion date for this project is 10/18/25 but hoping for an earlier completion date.




# Project Cost

- Property Purchase: \$900,000
- Dakota Redi Mix was the low bid on dirt work portion of the project at \$5,878,008. Change orders have added \$73,680 to the project for a total of \$5,951,688.
- McGough was the low bid on the structure/utilities portion of the project at \$11,953,688. No change orders have been executed to date.
- Design, Architectural and Engineering contracts total to date \$1,270,321.
- Total project cost: \$20,075,697.



# Changes in Design: JCA 2022

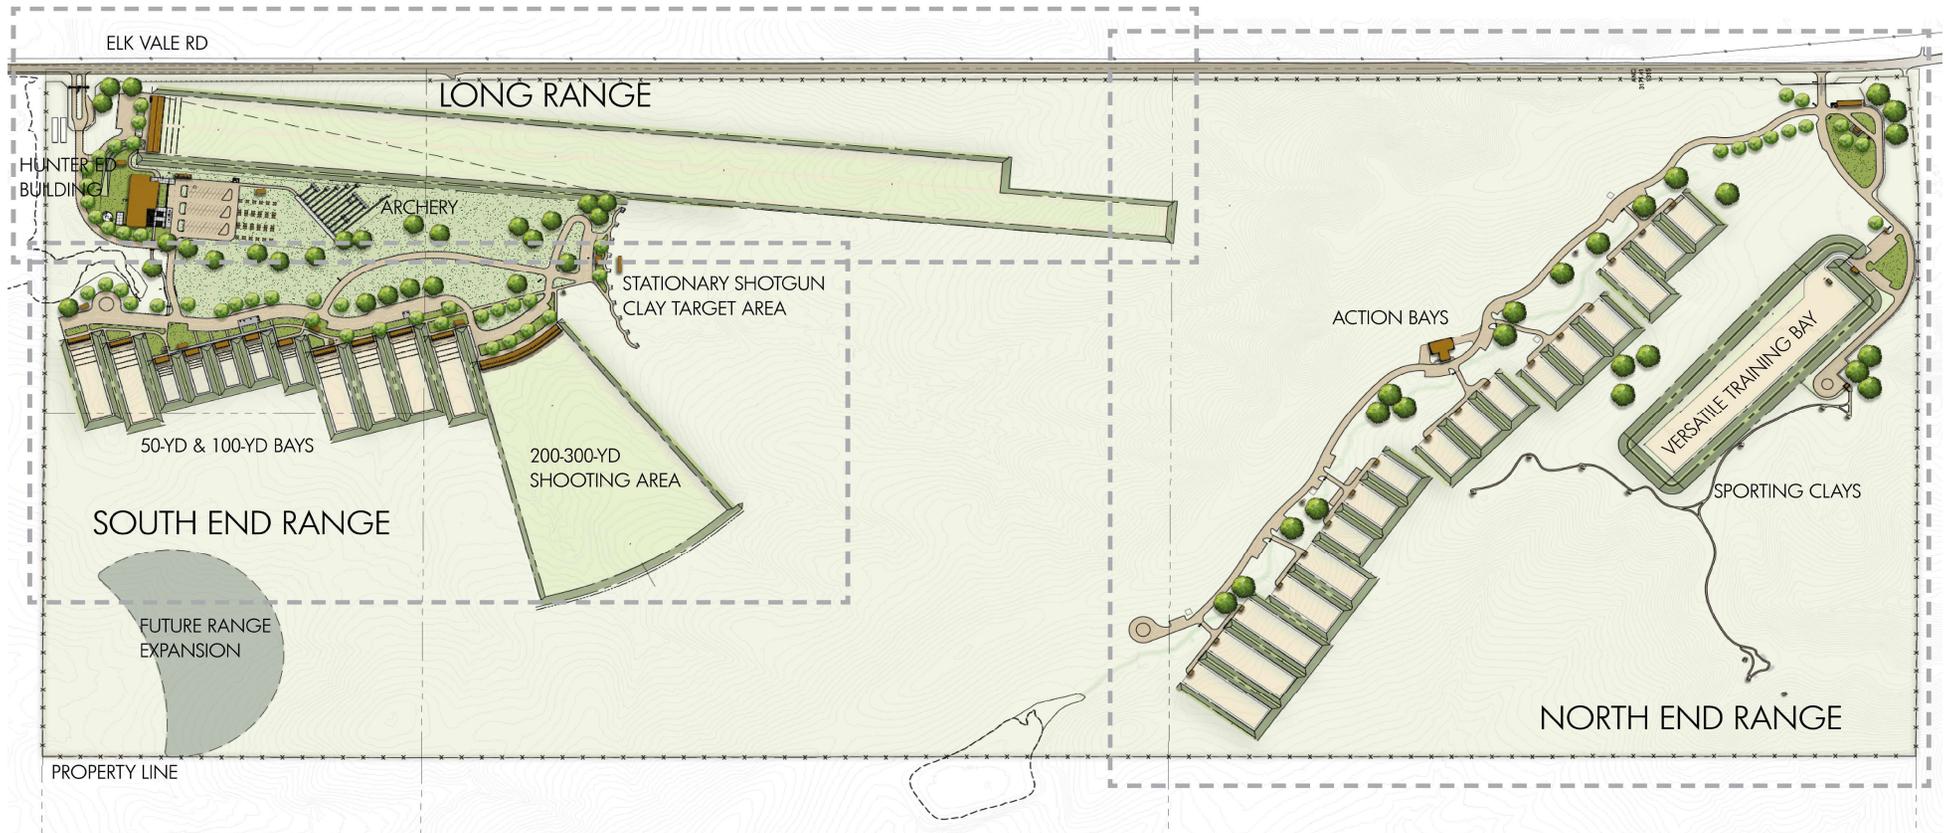

# Changes in Design as Bid in 2024



1. Relocated section line working with Meade County Commission (MCC).
  - a. The main entrance was reconfigured and associated infrastructure was reconfigured.
  - b. One 100-yard bay was removed and associated infrastructure was reconfigured.
  - c. A new county road was added to accommodate MCC desires.
2. The Hunting and Shooting Education Building (HSEB) was reduced in size.
3. The kitchen in the HSEB was upgraded to a commercial grade kitchen.
4. The shotgun area was redesigned to expand to allow for addition shotgun shooting disciplines (bunker trap, skeet, 5 stand, etc.).
5. The north range action bays were redesigned and repositioned to accommodate Meade County Ordinance 56 enacted by the MCC.



# Fund Sources and Expenditures

## Sources

- \$13,500,000 Future Fund Grant
- \$6,501,997 in private donations
- Additional private donations in progress

## Expended

- \$6,113,056 Invoiced to Date
- \$2,584,462.91 Future Funds used since grant award in April 2024



